



Executive Director's Report Paul Rainwater

March 18, 2009



Federal Officials' Visit

HUD Secretary Donovan and DHS Secretary Napolitano visited New Orleans on March 5

- Toured SUNO and the Lower 9th Ward in New Orleans and parts of St. Bernard Parish



*HUD Secretary Donovan, DHS Secretary Napolitano and FEMA Administrator nominee Craig Fugate in New Orleans
Photo source: The Associated Press*



Federal Officials' Visit

While in New Orleans, Secretary Donovan made the following announcements:

HUD

- Approved the state's \$438 million Gustav & Ike Action Plan
- Will launch, with the state, a new five-year, \$50 million program to offer permanent supportive housing to approximately 1,000 homeless individuals and families living with disabilities
- Will also provide \$23 million in rental assistance vouchers to the LRA to support an estimated 2,000 elderly and disabled disaster victims

2



Federal Officials' Visit

While in New Orleans, Secretary Napolitano made the following announcements:

DHS/FEMA

- Will provide Public Assistance Funding for Fire Stations #5 and #7 and Benjamin Franklin High School in New Orleans
- Will also provide \$12 million in additional funding to help repair the St. Bernard Parish Water Treatment Plant
- Two new joint review teams will be created, comprised of FEMA and state personnel, which will be tasked with quickly and fairly resolving disputes under the PA program
- Extended the Relocation Assistance Program to May 1, 2009

3



Washington Update

- Florida Emergency Management Director **Craig Fugate nominated to be the new FEMA Administrator**
Mr. Fugate joined the tour in New Orleans on Mar. 5
- On Mar. 11, DHS Secretary Napolitano announced the establishment of the Unified Public Assistance Project Decision Team, or the **“Louisiana Team”**
 - Created jointly by DHS and the State of Louisiana
 - FEMA Disaster Assistance Division Director Charlie Axton chosen to lead the team
 - Expedite final decisions to approve project scopes and eligible work costs for disputed projects
 - State estimates we have more than \$1 billion in FEMA projects under appeal or under dispute
- **Tony Russell named as the acting director of the Louisiana Transitional Recovery Office**

4



DHAP – Case Management

- HUD created the Transitional Assistance program, which extended DHAP through August 31, 2009
- **Request from HUD for state to administer the case management component of the program**
- **The state asked HUD and FEMA to consolidate this effort** with proposed case management for those still in FEMA temporary units (trailers and hotels), given the short timeframe and administrative challenges

5



DHAP – Case Management

- HUD informed the state on Mar. 12 that it **cannot include the FEMA trailer households** and asked the state to move forward with DHAP case management
- HUD did promise to find a way to include these families in the future
- Because 75% of the trailer residents are homeowners, the **state will continue to request that FEMA realign the funds** set aside for case management **to develop a Construction Management Pilot Program**

6



Gustav and Ike Update

as of Mar. 12, 2009

<h3 style="color: red;">Individual Assistance</h3> <h4 style="text-decoration: underline;">Gustav</h4> <p>440,907 registered in 53 declared parishes</p> <p><i>Housing Assistance</i></p> <ul style="list-style-type: none"> • 39,330 approved • 96 pending • \$160,134,956 distributed <p><i>Other Needs Assistance</i></p> <ul style="list-style-type: none"> • 57,700 approved • 191 pending • \$50,892,925 distributed 	<h4 style="text-decoration: underline;">Ike</h4> <p>53,903 registered in 20 declared parishes</p> <p><i>Housing Assistance</i></p> <ul style="list-style-type: none"> • 10,280 approved • 23 pending • \$51,486,086 distributed <p><i>Other Needs Assistance</i></p> <ul style="list-style-type: none"> • 5,243 approved • 32 pending • \$9,626,840 distributed
---	--

Gustav and Ike Debris Removal

Removed to date: **10 million cubic yards (99%)**

Remaining debris: **61,037 cubic yards (-42.7% from February)**

7

Gustav/Ike Housing Assistance

FEMA Housing Update:

- 9,437** - Households with damages greater than \$10,000
(based on FEMA IA Damage Inspections)
- 683** - FEMA Temporary Housing Units approved
- 424** - FEMA Temporary Housing Units on the ground
- 20** - Parishes where the FEMA Temporary Units have been placed



Flooding in Cocodrie, LA, after Hurricane Gustav

as of Mar. 9, 2009 8

Public Assistance Update

	Applicants	Projects	Obligated	Paid*
Katrina	2,161	17,942	\$6.92 billion	\$ 3.82 billion
Rita	931	4,468	\$573 million	\$ 407 million
Gustav	1,072	1,014	\$320 million	\$110 million <i>(was \$9.23 million)</i>
Ike	409	309	\$46 million	\$12.9 million <i>(was \$273,582)</i>



Public Assistance Express Pay**

As of Mar. 12, 2009, the Express Pay program has processed **4,742 RRFs** paying out **\$835,272,090** to applicants.

Average payment time is currently **8 business days**.

***will also use Express Pay for Gustav and Ike projects*

*as of Mar. 12, 2009 9

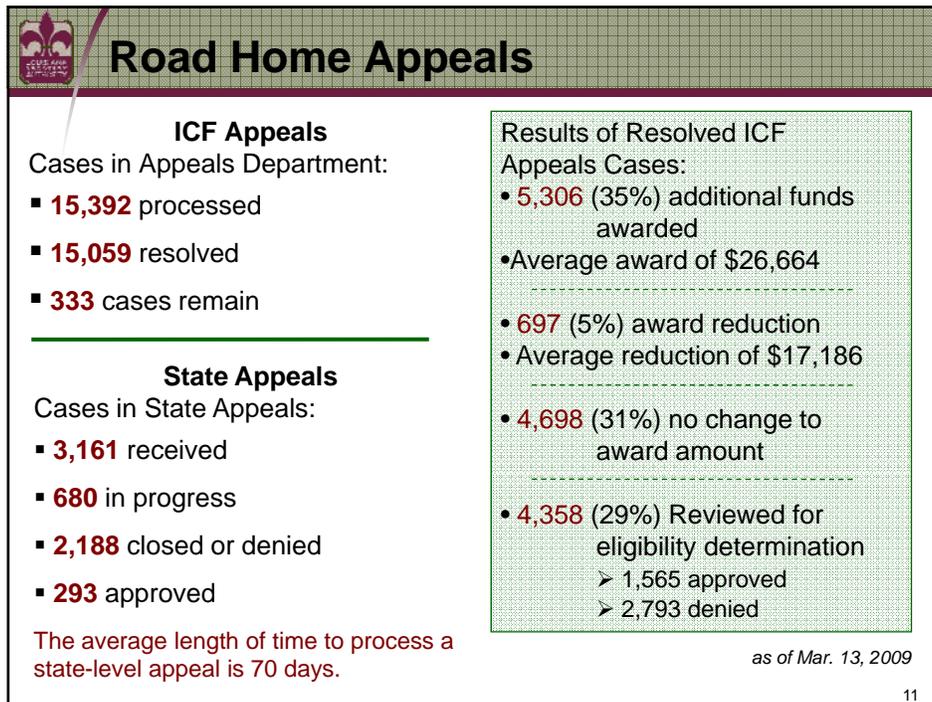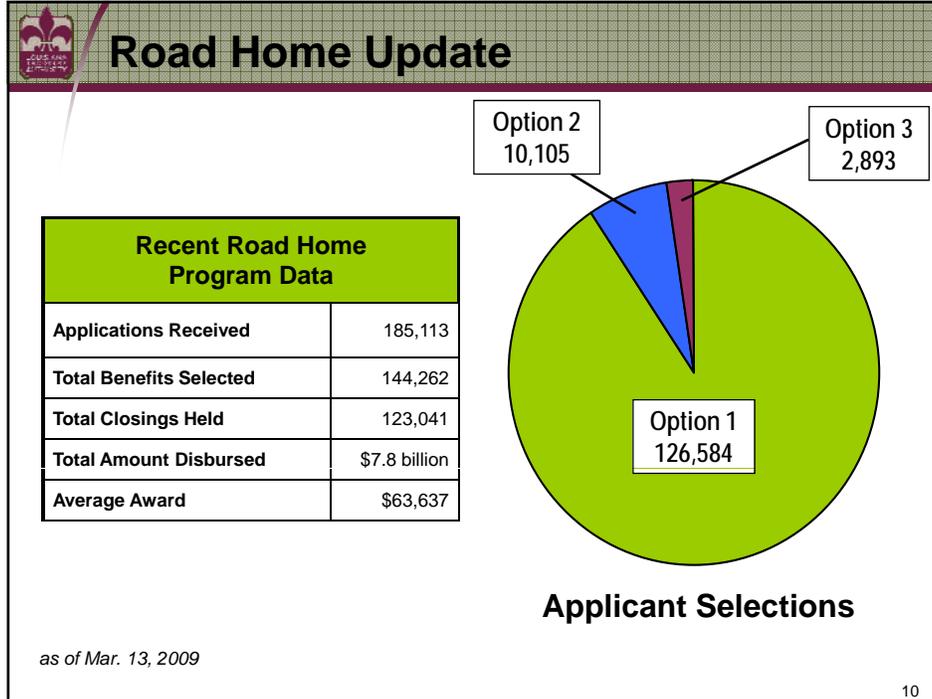

 **CDBG/Road Home Elevations**



As of 3/13/09:

- **30,406** homeowners interested in and eligible for elevation program
- **26,348** elevation disbursements awarded
- **\$762.8 million** disbursed
- **1,083 (\$30.6 million)** elevation disbursements at closing companies

A home in Lakeview in New Orleans elevated through the Road Home Elevation program

12

 **HMGP Elevations**

as of Mar. 13, 2009

- **20,791** people interested
- **1,604** files being worked
- **519** homeowner meetings completed
- **14** homeowner mid-point payments made totaling **\$177,859**

(was 3 midpoint payments totaling \$39,431)



An elevated home in Gentilly

13

Louisiana Land Trust

New Orleans:

- NORA – 37 properties ready for transfer
 - **The first 6 properties closed on Mar. 6** (soft opening)
 - Balance of the 31 properties in the first group are either awaiting financing or were transferred to Make It Right the week of Mar. 9
- NORA and LLT are reviewing a priority list of 200 properties in need of demolition before transfer
- Approximately 3,800 have received environmental clearance

St. Tammany Parish:

- CEA signed by the parish, LLT and OCD
- Parish is developing priority transfer list
- Parish working on Land Bank

Louisiana Land Trust

LLT Transfer Timeline

Demolition management company is in place

Working with parishes to identify properties for demolition

14

Louisiana Land Trust

Jefferson Parish:

- Waiting for environmental to be signed off on
- LLT has begun process to transfer 29 properties ASAP
- OCD to put properties back into commerce as affordable housing

▪ Seven additional lots will be transferred to OCD for affordable housing

- Lots have structures that must be demolished before the property can be transferred

▪ Parish demolition list was sent to Louisiana Solutions

- Title work ordered on properties requested
- Parish working to finalize the “Lot Next Door” program in a timely manner

St. Bernard Parish:

- Parish contractor developing disposition list

Terrebonne Parish:

- Parish developing demolition list

Cameron Parish:

- Met with parish officials on Mar. 2 to discuss disposition priorities
- Awaiting parish request

Calcasieu Parish:

- Parish disposition plan approved at Feb. 26 LRA Board meeting
- Transfer CEA signed by parish, executed by LLT on Mar. 9 and sent to OCD for signature

15



Small Rental Program

• Active awardees	5,859
• Rental closings	480
• Rental award amount	\$38.80 million
• Units produced	1,073
• Affordable units produced	756

as of Mar. 12, 2009

16



LIHTC/CDBG Piggyback Program



•Total projects awarded:		57
•Total units awarded:		8,185
•Total award amount:		\$596 million
•Projects closed/ under construction:		21
•Units under construction:		3,476
•Dollars closed:		\$311 million
•Dollars expended:		\$159 million
•Projects completed:		3
•Total amount:		\$47.8 million
•Units completed		355

as of Mar. 13, 2009

The Meridian in New Orleans

17



LIHTC/CDBG Piggyback Program

- **695 units** available by the end of the month
- **Two grand openings** held Mar. 10 in New Orleans
 - The Preserve – 183 mixed-income units**
 - The Meridian – 72 affordable units*
- **Two grand openings this week**
 - 200 Carondelet in New Orleans – 190 mixed-income units**
 - Tiffany Apartments in Abbeville – 250 mixed-income units**
- Anticipate over **1,800 units** online by June 2009
- A total of **3,200 units** online by **Dec. 31, 2009**

*All mixed-income units are 60% market rate and 40% affordable



Walter Leger speaking at The Preserve ribbon-cutting/grand opening on Mar. 10.

18



Alternative Housing Pilot Program

- After expressing concern about the delayed environmental approval dates, FEMA has expedited completion
- Expect a production schedule for the 200 modular units this week, which will allow us to begin ordering from the modular manufacturers

New Orleans – 287 units

- 100 single-family units in Algiers
- 100 units on infill sites in various neighborhoods
- 27 single-family units in Westwego – **CEA should be complete this week; ready to begin infrastructure immediately after**
- 60 units as infill sites in Tremé Neighborhood
- Construction expected to begin in April

Jackson Barracks - 93 units

- Infrastructure complete in early April
- Single-family construction began in February
- Multi-family construction begins in April
- Construction complete by August

504 total units



Progress being made at the Jackson Barracks single-family construction site

as of Mar. 13, 2009
19

 **Alternative Housing Pilot Program**

Eight frames are up at the Hidden Cove site in Baton Rouge

Baton Rouge – 42 units

- All foundations poured, with the exception of the 5 lots exchanged with BREC (swap made to better accommodate the project and recreation)
- Framing up for 8 homes
- Construction complete by July

Lake Charles – 82 units

- 34-units group site sale closed for \$538,000 using United Way funds
- Bid on construction of the 34-unit group was awarded Mar. 13
- Construction will begin on that group the week of Mar. 23
- Construction expected to begin in April



as of Mar. 13, 2009

20

 **ICF Transition Team**

ICF Transition Team is procuring RFPs and recommending contractors for

- **IT**
- **Homeowners**
- **Small Rental**
- **Piggyback**
- **HMGP**
- **IMM**

21



ICF Transition Team

IT

- The state announced Feb. 26 that **CGI Technologies & Solutions** was awarded the IT contract
- The contract has been negotiated and signed
- Contract being reviewed for approval by the State Procurement Office

Homeowners

- The state announced Feb. 26 that **Hammerman and Gainer, Inc. (HGI)** was awarded the Homeowners contract
- Contract negotiations are underway
- Goal to have contract signed by both parties no later than Mar. 20

Small Rental

- The state announced Mar. 12 that **ACS State and Local Solutions, Inc.**, was awarded the Small Rental contract

22



ICF Transition Team

Piggyback
Two proposals received

HMGP
RFPs deadline was March 9

IMM
Currently in the advertising phase

23



HVAC Generator Program

- The state has set aside **\$30 million in federal HMGP funding for program**
- Will help **hospitals and nursing homes purchase “HVAC generators” to power air conditioning** during major power outages
- **Will also equip the Louisiana State Emergency Medical Special Needs Shelter** with an HVAC generator system
- **Allocation of funding:**
 - \$19.6 million for nursing homes
 - \$ 8.4 million for hospitals
 - \$ 2 million for the Louisiana State Emergency Medical Special Needs Shelter
- Funds made **available statewide**
- State will **reimburse up to 75% of the cost** to obtain the HVAC Generator
